

Goal Directed Planning (GDP)


Lloydmasters' Goal Directed Planning process gains

peoples' involvement, alignment, commitment, ownership and teamwork in order to deliver a desired project outcome

Traditional methods focus on techniques, tools and 'hard' analysis to deliver programmes, activity lists and schedules

The process effectively engages participants to build shared understanding of key system goals and generates ownership and commitment in the delivery

Illustrative Goal Directed Plan
Project team: JOJ, MB, PM, DM, CP, LH, RG, FN
Diagram Version ID: Illustrative

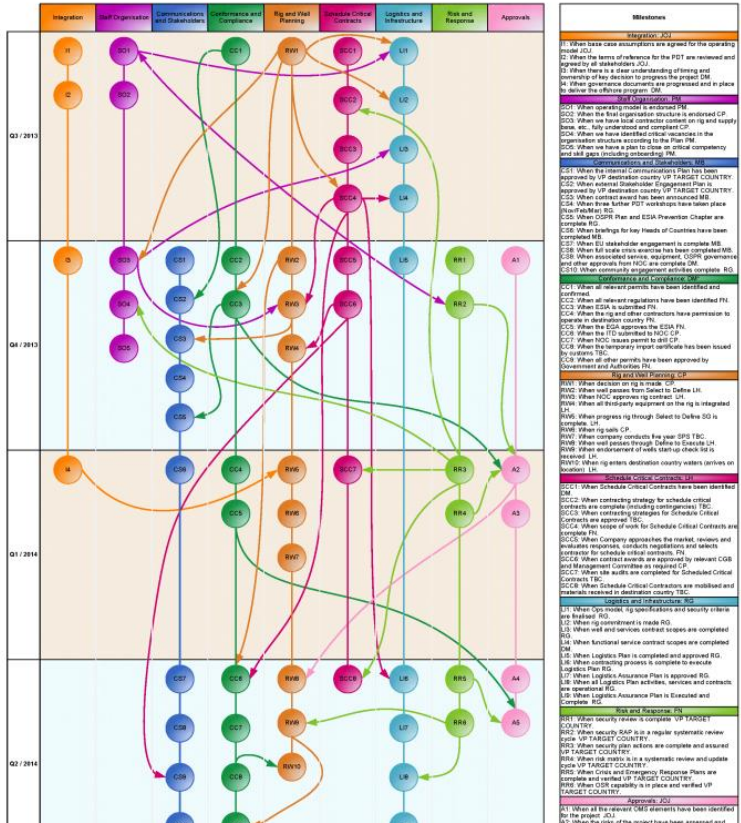

Integration	Staff Organisation	Communication and Stakeholders	Confirmation and Compliance	Rig and Well Planning	Schedule Critical Contracts	Logistics and Infrastructure	Risk and Response	Approvals	
<p>1 When base case assumptions are agreed for the operating mode</p> <p>2 When the terms of reference for the JCI are reviewed and agreed by all stakeholders</p> <p>3 When there is a clear understanding of being and ownership of key decisions to progress the project</p> <p>4 When governance documents are prepared and in place to deliver the offshore program</p> <p>5 When we have a plan to deliver the offshore program</p>	<p>SO1 When operating model is endorsed</p> <p>SO2 When the first regulatory structure is endorsed</p> <p>SO3 When we have clear understanding of being and ownership of key decisions to progress the project</p> <p>SO4 When we have identified critical stakeholders in the project</p> <p>SO5 When we have a plan to deliver the offshore program</p>	<p>CS1 When the external Communication Plan has been approved by VP destination country</p> <p>CS2 When external Stakeholder Engagement Plan is approved by VP destination country</p> <p>CS3 When contract award has been announced</p> <p>CS4 When three further JCI workshops have been placed (two for the JCI)</p> <p>CS5 When OPR Plan and CSA Revision Chapter are complete</p> <p>CS6 When the final scale cost review has been completed</p> <p>CS7 When EU state-aid is complete</p> <p>CS8 When full scale cost review has been completed</p> <p>CS9 When associated services, equipment, OPR governance and other approvals from NOC are complete</p> <p>CS10 When community engagement activities complete</p>	<p>CC1 When all relevant permits have been identified and confirmed</p> <p>CC2 When all relevant regulations have been identified</p> <p>CC3 When ESA is submitted</p> <p>CC4 When the rig and other contractors have permission to operate in destination country</p> <p>CC5 When the ESA approves the ESA</p> <p>CC6 When the temporary permit certificate has been issued by customs</p> <p>CC7 When NOC contract is complete</p> <p>CC8 When the temporary permit certificate has been issued by customs</p> <p>CC9 When all other permits have been approved by Government and Authorities</p> <p>CC10 When destination country waters carries on location</p>	<p>DP1 When decision on rig is made</p> <p>DP2 When well permit from Select to Define is approved</p> <p>DP3 When NOC contract is complete</p> <p>DP4 When progress rig through Select to Define is complete</p> <p>DP5 When rig starts</p> <p>DP6 When contract award has been announced</p> <p>DP7 When contract award has been announced</p> <p>DP8 When contract award has been announced</p> <p>DP9 When contract award has been announced</p> <p>DP10 When contract award has been announced</p>	<p>SC1 When Schedule Critical Contracts have been identified</p> <p>SC2 When contracting strategy for schedule critical contracts is complete</p> <p>SC3 When contracting strategy for schedule critical contracts is complete</p> <p>SC4 When contracting strategy for schedule critical contracts is complete</p> <p>SC5 When contracting strategy for schedule critical contracts is complete</p> <p>SC6 When contracting strategy for schedule critical contracts is complete</p> <p>SC7 When contracting strategy for schedule critical contracts is complete</p> <p>SC8 When contracting strategy for schedule critical contracts is complete</p> <p>SC9 When contracting strategy for schedule critical contracts is complete</p> <p>SC10 When contracting strategy for schedule critical contracts is complete</p>	<p>LI1 When rig contract is made</p> <p>LI2 When well and services contract scopes are complete</p> <p>LI3 When functional service contract scopes are complete</p> <p>LI4 When Logistics Plan is complete and approved</p> <p>LI5 When Logistics Plan is complete and approved</p> <p>LI6 When Logistics Plan is complete and approved</p> <p>LI7 When Logistics Plan is complete and approved</p> <p>LI8 When Logistics Plan is complete and approved</p> <p>LI9 When Logistics Plan is complete and approved</p> <p>LI10 When Logistics Plan is complete and approved</p>	<p>RR1 When security review is complete</p> <p>RR2 When security review is complete</p> <p>RR3 When security review is complete</p> <p>RR4 When security review is complete</p> <p>RR5 When security review is complete</p> <p>RR6 When security review is complete</p> <p>RR7 When security review is complete</p> <p>RR8 When security review is complete</p> <p>RR9 When security review is complete</p> <p>RR10 When security review is complete</p>	<p>A1 When all relevant permits have been identified and confirmed</p> <p>A2 When the risks of the project have been assessed and approved</p> <p>A3 When all relevant permits have been identified and confirmed</p> <p>A4 When all relevant permits have been identified and confirmed</p> <p>A5 When all relevant permits have been identified and confirmed</p> <p>A6 When all relevant permits have been identified and confirmed</p> <p>A7 When all relevant permits have been identified and confirmed</p> <p>A8 When all relevant permits have been identified and confirmed</p> <p>A9 When all relevant permits have been identified and confirmed</p> <p>A10 When all relevant permits have been identified and confirmed</p>	
When the JCI is working as an integrated team and decisions are made in line with the Plan	When we have the required capability at the right time for 1 July SPUD	When all stakeholders and team are fully engaged, supportive and committed	When all stakeholders and team are fully engaged, supportive and committed	When required permits to DR are approved	When Go/No-Go decision is made	When all services and materials are sourced in support of a 1 July SPUD	When all logistics, services, equipment and bases are ready to operate at the Go/No-Go decision point	When identified risks are assessed and the response capability is designed, implemented and tested as ready to operate	When the planned operations conform to OMS based on risk profile
